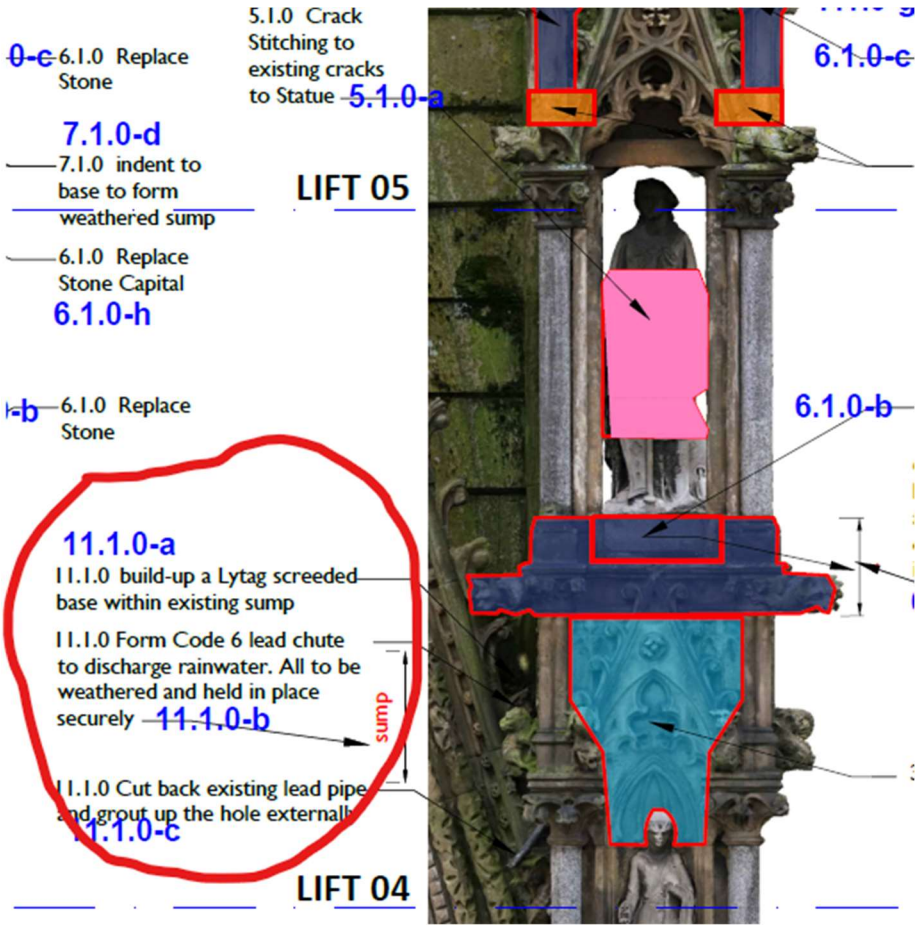
SITE RECORD SHEET

PURCELL


Aconex Ref: OTH-PUR-TH-ZZ-SRS-A-0618	**Date:** 15/05/2024
Document Title: Albert Memorial – Omission of Works	**Revision:** -
Visit By: Jamie Coath, Andrew Bailey (Purcell), John Tomlin (LL), Steve Eccleshare (Bullen)	**Status: -** For Information
Attended: See below sections	**Attachments:** Photos embedded where applicable

No	Item/Room	Comments	Action
		Following site review on 25.04.24, a series of originally proposed works are deemed no longer required.	
1.1	Albert Memorial – Sump Behind Corner Pinnacles	Following discussions on site, it was agreed that the proposed lead chute detail (to be formed onto a new Lytag screed base), which sits behind each of the corner pinnacles (4 nr. in total), is to be omitted. The existing sump and drainpipe arrangement is to be retained. Both sump and drainpipe have been cleared out and are now draining freely. Extract from Purcell drawing OTH-PUR-EE-ZZ-DWG-A-7143. Items to be omitted (circled in red) are 11.1.0a, 11.1.0b, 11.1.0c. 	


Checklist:

Active Work/ Upcoming Work	Clerk of Works items to note	Number of People Working on Site
Progress Against Programme	Review with JC or other	Site Safety Issues
Quality of Work/ Defective Work	Materials on Site/ Storage/ Quality	Test Certificates/ RAMS reviewed
Any change from contract work to note	Heritage Surgery notes	Aconex uploaded (check off once uploaded)
RFI answered	Samples Approved/ Rejected	

Extract from Purcell drawing OTH-PUR-EE-ZZ-DWG-A-7144. Items to be omitted (circled in red) are 11.1.0a, 11.1.0b, 11.1.0c.

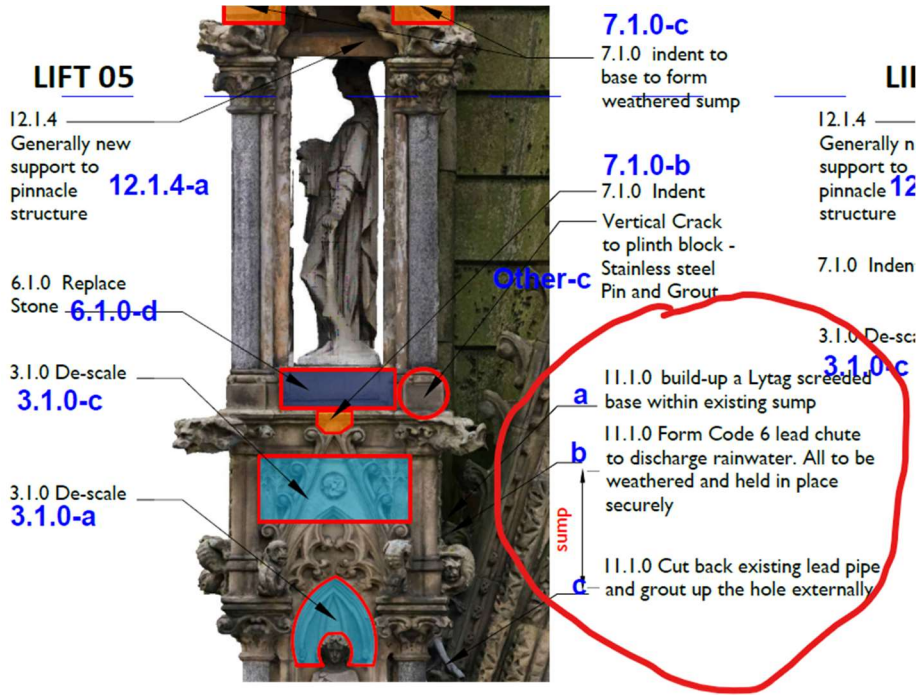

Extract from Purcell drawing OTH-PUR-EE-ZZ-DWG-A-7145. Items to be omitted (circled in red) are 11.1.0a, 11.1.0b, 11.1.0c.

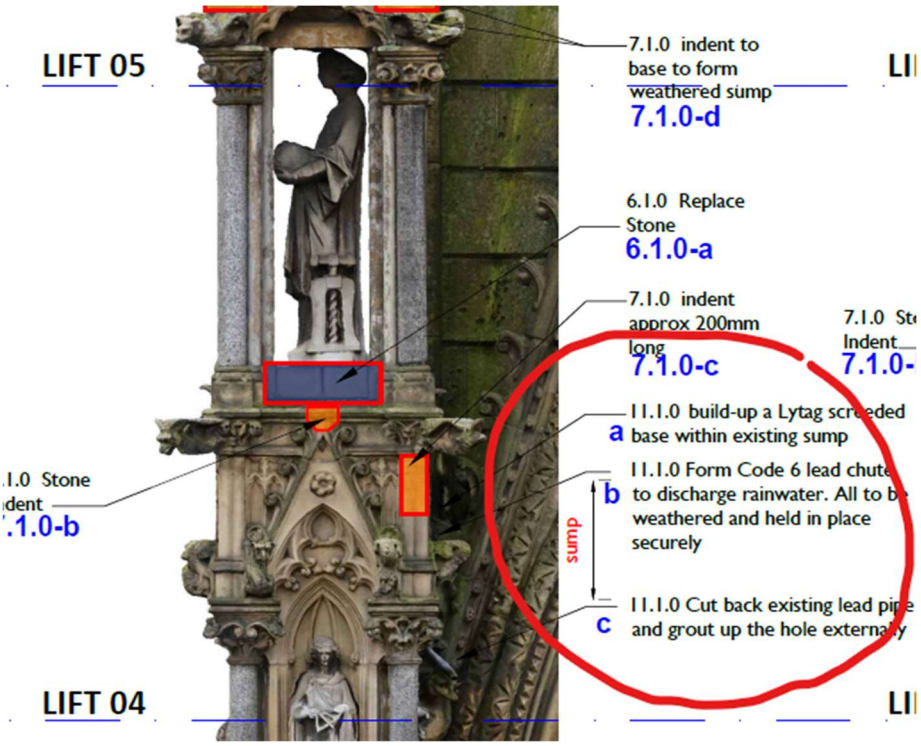

Extract from Purcell drawing OTH-PUR-EE-ZZ-DWG-A-7146. Items to be omitted (circled in red) are 11.1.0a, 11.1.0b, 11.1.0c.

