
INSERT TRUST LOGO HERE

Christie ASICD
Main Build Programme 02

Integrated Health Projects by VINCI BUILDING Sir Robert McALPINE

Line	Task ID (WBN)	Name	Start	Working Duration	Finish
1	28210	**Design and Commercial**	Thu 11/07/24 A	110w 3d	Mon 05/10/26
2	25880	Trust Approve RIBA 3 and Agree Future Funding	Mon 01/09/25 A	4w	Fri 26/09/25 A
3	33650	Update Model	Mon 02/06/25 A	1w	Fri 06/06/25 A
4	33640	Incorporate Stage 3 Changes following review	Mon 09/06/25 A	2w	Fri 20/06/25 A
5	33670	VE	Mon 29/09/25 A	2w	Fri 10/10/25 A
6	38360	Stage 3 Plus	Mon 07/07/25 A	18w	Fri 07/11/25 A
7	36270	Stage 4 Surveys	11 Jul 24 A	71w	11 Dec 25
8	25890	RIBA 4 Design	Mon 02/06/25 A	29w	Fri 19/12/25 A
9	38340	RIBA Stage 4 Approval	Mon 05/01/26 A	4w	Fri 30/01/26
10	38310	Final Model Co-ordination	Mon 05/01/26 A	4w	Fri 30/01/26
11	38650	Route To Affordability	Tue 17/02/26	10w	Tue 05/05/26
12	38590	**Kick Off Meeting**	Tue 17/02/26 *		Tue 17/02/26
13	38320	**Develop VE Schedule**	Tue 17/02/26 *	2w	Mon 02/03/26
14	38610	**Client Review Meeting**	Tue 03/03/26	1d	Tue 03/03/26
15	38620	**Pricing Information Produced**	Wed 04/03/26	5w 4d	Mon 20/04/26
16	38630	**Supply Chain Pricing**	Tue 21/04/26	2w	Mon 04/05/26
17	38640	**Client Instruction For Changes To Be Made**	Tue 05/05/26		Tue 05/05/26
18	38660	Client Changes	Tue 17/02/26	10w	Tue 05/05/26
19	38680	**Kick Off Meeting**	Tue 17/02/26 *		Tue 17/02/26
20	38690	**Develop Client Change Schedule**	Tue 17/02/26 *	2w	Mon 02/03/26
21	38700	**Client Review Meeting**	Tue 03/03/26	1d	Tue 03/03/26
22	38710	**Pricing Information Produced**	Wed 04/03/26	5w 4d	Mon 20/04/26
23	38720	**Supply Chain Pricing**	Tue 21/04/26	2w	Mon 04/05/26
24	38670	**Client Instruction For Changes To Be Made**	Tue 05/05/26		Tue 05/05/26
25	38350	VE And Client Stage 4 Re-design (Duration TBC)	Tue 05/05/26	6w	Mon 15/06/26
26	38990	**CDE To Move To Dalux**	Tue 16/06/26		Tue 16/06/26
27	36380	**Submit Building Control Initial Notice**	Wed 04/03/26 *		Wed 04/03/26

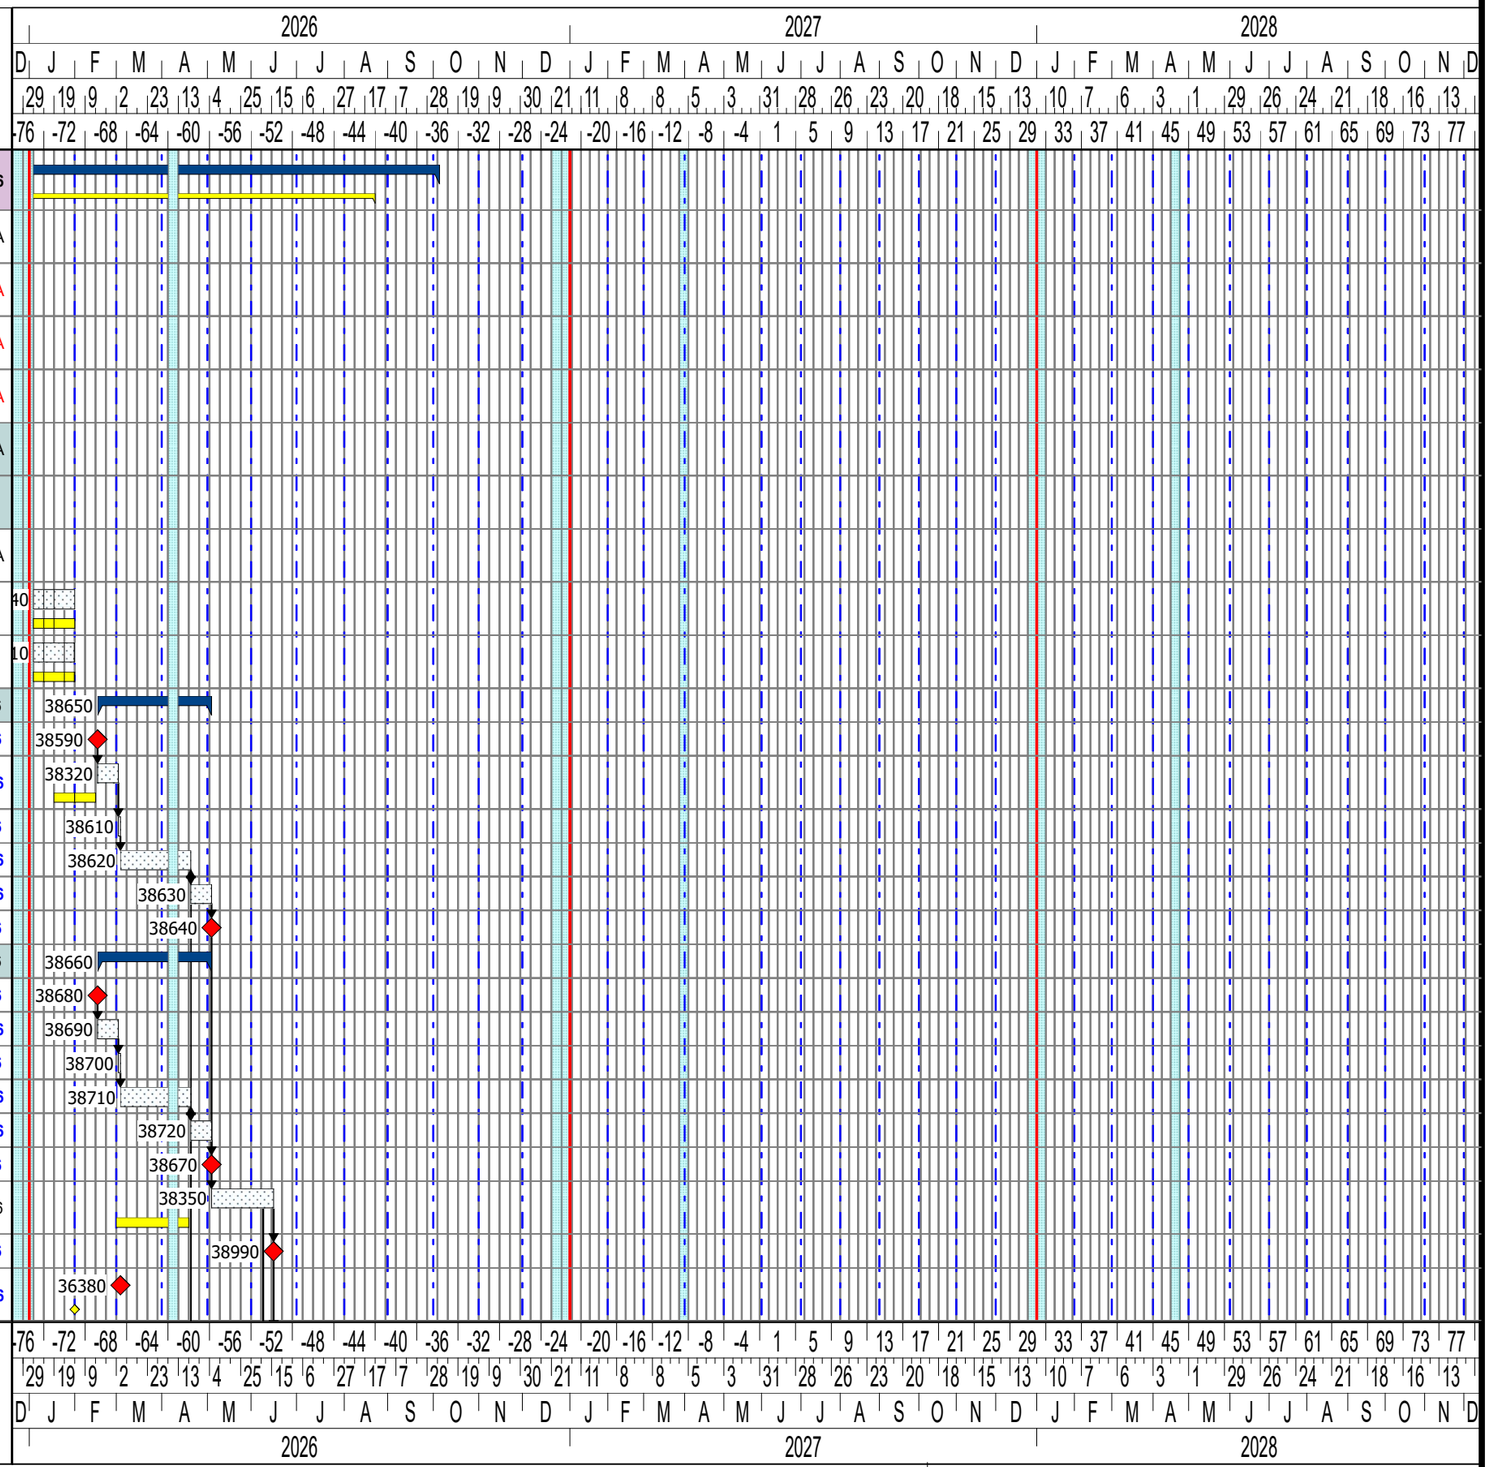

Programme No: HH0075/ST4 Draft		**Christie Main Build Pre Con**	Programme Status:
Revision: REV2	Date 19/03/2026		Prepared For (Owner): PD
Rev Comment:			Drawn By (Planner): LF
			Region: North West / Progress Date: 28/02/2026


'Note that the Duration Column Shows Working Weeks and Does Not Include Holidays'

INSERT TRUST LOGO HERE

Christie ASICD
Main Build Programme 02

Integrated Health Projects by VINCI BUILDING Sir Robert McALPINE

Line	Task ID (WBN)	Name	Start	Working Duration	Finish
28	38730	Building Control RIBA Stage 4 Plan Review	Tue 16/06/26	2w	Mon 29/06/26
29	**38370**	**Stage 4 Cost Update**	**Mon 19/01/26 A**	**12w 1d**	**Mon 20/04/26**
30	38380	Commence Target Price Update Based On RIBA Stage 4 - Bill Developement	Tue 09/06/26	12w	Mon 31/08/26
31	38390	IHP Adjudication	Tue 01/09/26	1w	Mon 07/09/26
32	25910	FBC Development & Approval	Tue 16/06/26	16w	Mon 05/10/26
33	38980	Expiration of Building Control If GF Slab Incomplete	Mon 05/03/29 *		Mon 05/03/29
34	**36430**	**Pre-Commencement Conditions**	**Mon 11/03/24 A**	**235w 1d**	**Mon 11/12/28**
35	38780	Meaningful Start Pre Commencement Conditions	Mon 11/03/24 A	164w 3d	Wed 14/07/27
36	36440	Tree Re-Location - Condition 14	Mon 13/10/25 A	17w 4d	Fri 27/02/26 A
37	36450	Condition 4. Site Investigation Report and Remediation Strategy	Mon 11/03/24 A	97w 1d	Mon 02/03/26
38	36470	Condition 6. Sustainable Drainage Scheme	Fri 19/12/25 A	8w	Thu 26/02/26 A
39	36460	Condition 17. Demolition and Construction Management Plan (DCMP)	Fri 19/12/25 A	8w	Fri 27/02/26 A
40	39050	Full Discharge (Pre Demo)	Mon 10/05/27	9w 2d	Wed 14/07/27
41	**39100**	**None Material Ammendment For Stage 4 Changes (Latest Date)**	**Mon 24/05/27 ***		**Mon 24/05/27**
42	38790	Above Ground Pre Commenement Condtions	Mon 27/09/27	60w	Mon 11/12/28
43	38840	Condition 3 Samples	Mon 27/09/27	8w	Mon 22/11/27
44	38890	Condition 15 Hard & Soft Landscaping	Mon 16/10/28	8w	Mon 11/12/28
45	38960	Tree Relocation	Mon 27/04/26	82w	Fri 10/12/27
46	**38280**	**Obtain Landowner Permission For Tree Re-Location**	**Mon 27/04/26 ***		**Mon 27/04/26**
47	**38950**	**Agree Strategy With Council For None Viable Trees (T2 & T4)**	**Mon 27/04/26**	**2w**	**Fri 08/05/26**
48	36540	Re-Locate 5 No Trees (T3 - T5-8)	Mon 04/01/27 *	3w	Fri 22/01/27
49	36700	Remove 1 No Tree (T1)	Mon 04/01/27 *	1w	Fri 08/01/27
50	36510	Monitoring & Aftercare (T3 - T5-T8)	Mon 25/01/27	45w	Fri 10/12/27
51	**34440**	**Actvities Associated with Discharging the 'Meanigful Start' Condition**	**Wed 27/08/25 A**	**17w 2d**	**Fri 09/01/26 A**
52	37570	Legal Confirmation - Deloitte compile evidence and seek legal advice to confirm that planning consent has been lawfully implemented	Mon 13/04/26 *	1w	Fri 17/04/26

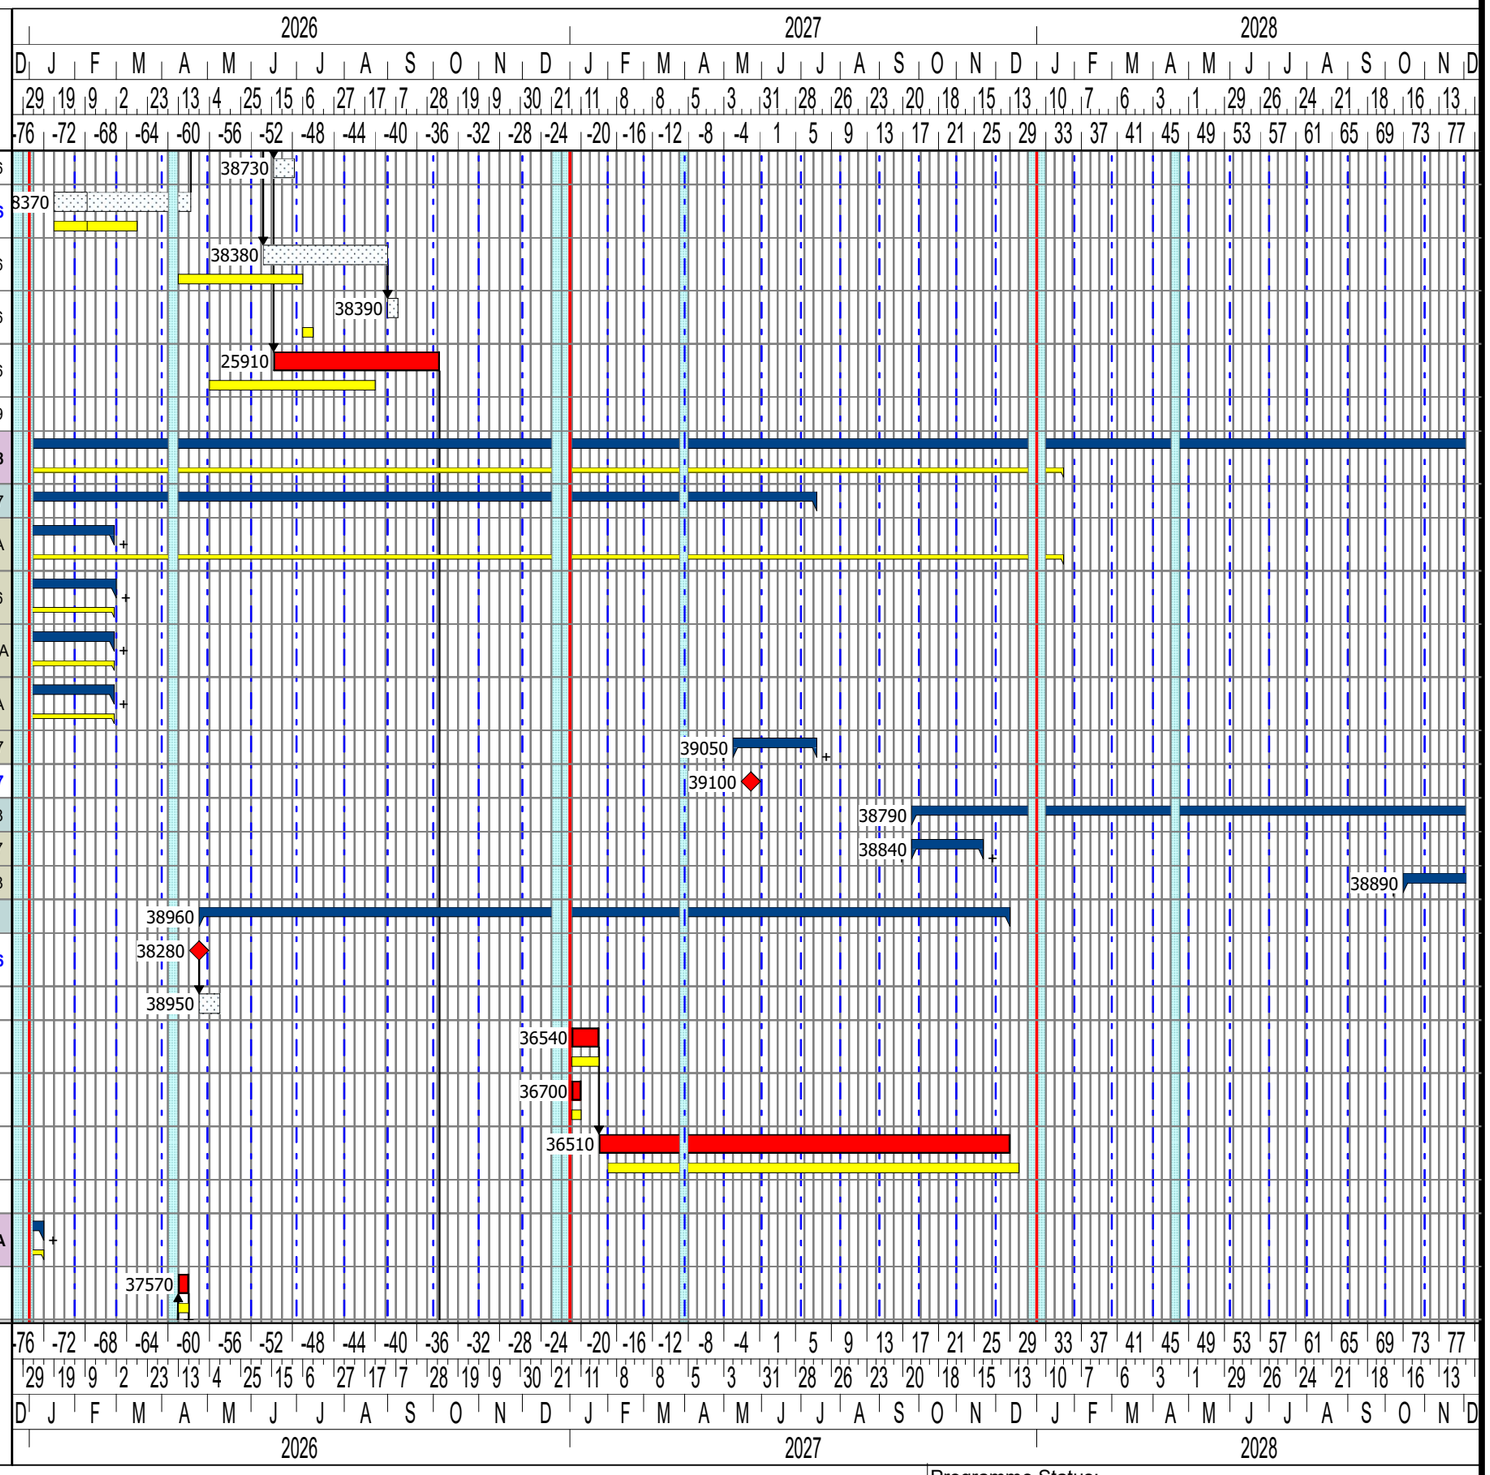

Programme No: HH0075/ST4 Draft		Programme Status:
Revision: REV2	Date 19/03/2026	Prepared For (Owner): PD
Rev Comment:		Drawn By (Planner): LF
		Region: North West / Progress Date: 28/02/2026

Christie Main Build Pre Con

'Note that the Duration Column Shows Working Weeks and Does Not Include Holidays'


Filename \\wat-fls-clstr13\Building\NorthWest\Projects\Current\HH0075 - Christie ASICD\14 Programme\Weekly Progress\Main Build Weekly Progress\Main Build Christie ASICD Rev 1 Progress 27.02.26.pp

INSERT TRUST LOGO HERE

Christie ASICD
Main Build Programme 02

Integrated Health Projects by VINCI BUILDING Sir Robert McALPINE

Line	Task ID (WBN)	Name	Start	Working Duration	Finish
53	37580	Submission to LPA and request documentation uploaded to public access system.	Mon 20/04/26		Mon 20/04/26
54	**26590**	**NOTE: Planning Approval Expires - 01.12.2026 (Change to 22.12.26)**	**Mon 14/12/26 ***		**Mon 14/12/26**
55	**38580**	**Meaningful Start Works**	**Mon 19/01/26 A**	**11w**	**Fri 03/04/26**
56	38500	Detail Design	Mon 19/01/26 A	6w	Fri 27/02/26
57	38510	Mobilisation	Mon 02/03/26	1w	Fri 06/03/26
58	38520	CFA Piling	Mon 09/03/26	1w	Fri 13/03/26
59	38530	Excavation & Ground Beam Fabrication & Formwork	Mon 16/03/26	1w	Fri 20/03/26
60	38540	Pile Cropping	Mon 23/03/26	1d	Mon 23/03/26
61	38550	Pile Integrity Testing	Tue 24/03/26	1d	Tue 24/03/26
62	38560	Cast Pile Caps & Ground Beams	Wed 25/03/26	1w	Tue 31/03/26
63	38570	Demobilise and clear site	Wed 01/04/26	3d	Fri 03/04/26
64	**38480**	**Decant Completion Dates**	**Mon 01/06/26**	**53w 4d**	**Mon 05/07/27**
65	**39130**	**002B (IHP Bio Bank) - CSSS Office Relocation (Network Management) Paterson Tail 2nd Floor**	**Mon 01/06/26 ***		**Mon 01/06/26**
66	**38400**	**(IHP) - Paterson Tail - 1st Floor - Research Radiotherapy Fit-Out**	**Tue 07/07/26 ***		**Tue 07/07/26**
67	**38410**	**(IHP) - Paterson Tail - 1st Floor - Radiology**	**Tue 14/07/26 ***		**Tue 14/07/26**
68	**38420**	**005 (IHP) - Paterson Tail - Ground Floor - Office Fit-Out - Trust Execs**	**Mon 03/08/26 ***		**Mon 03/08/26**
69	**38450**	**003 (IHP TBC) - Pre-Op Department**	**Fri 09/04/27 ***		**Fri 09/04/27**
70	**38440**	**001 (IHP) - Radiotherapy**	**Fri 04/06/27 ***		**Fri 04/06/27**
71	**38430**	**002D (IHP Bio Bank) - Bio Bank Lab Relocation**	**Mon 05/07/27 ***		**Mon 05/07/27**
72	**38460**	**002 (IHP) - Histology**	**Mon 05/07/27 ***		**Mon 05/07/27**
73	**26600**	**Main Works (IHP Programme)**	**Tue 06/10/26**	**19w**	**Mon 01/03/27**

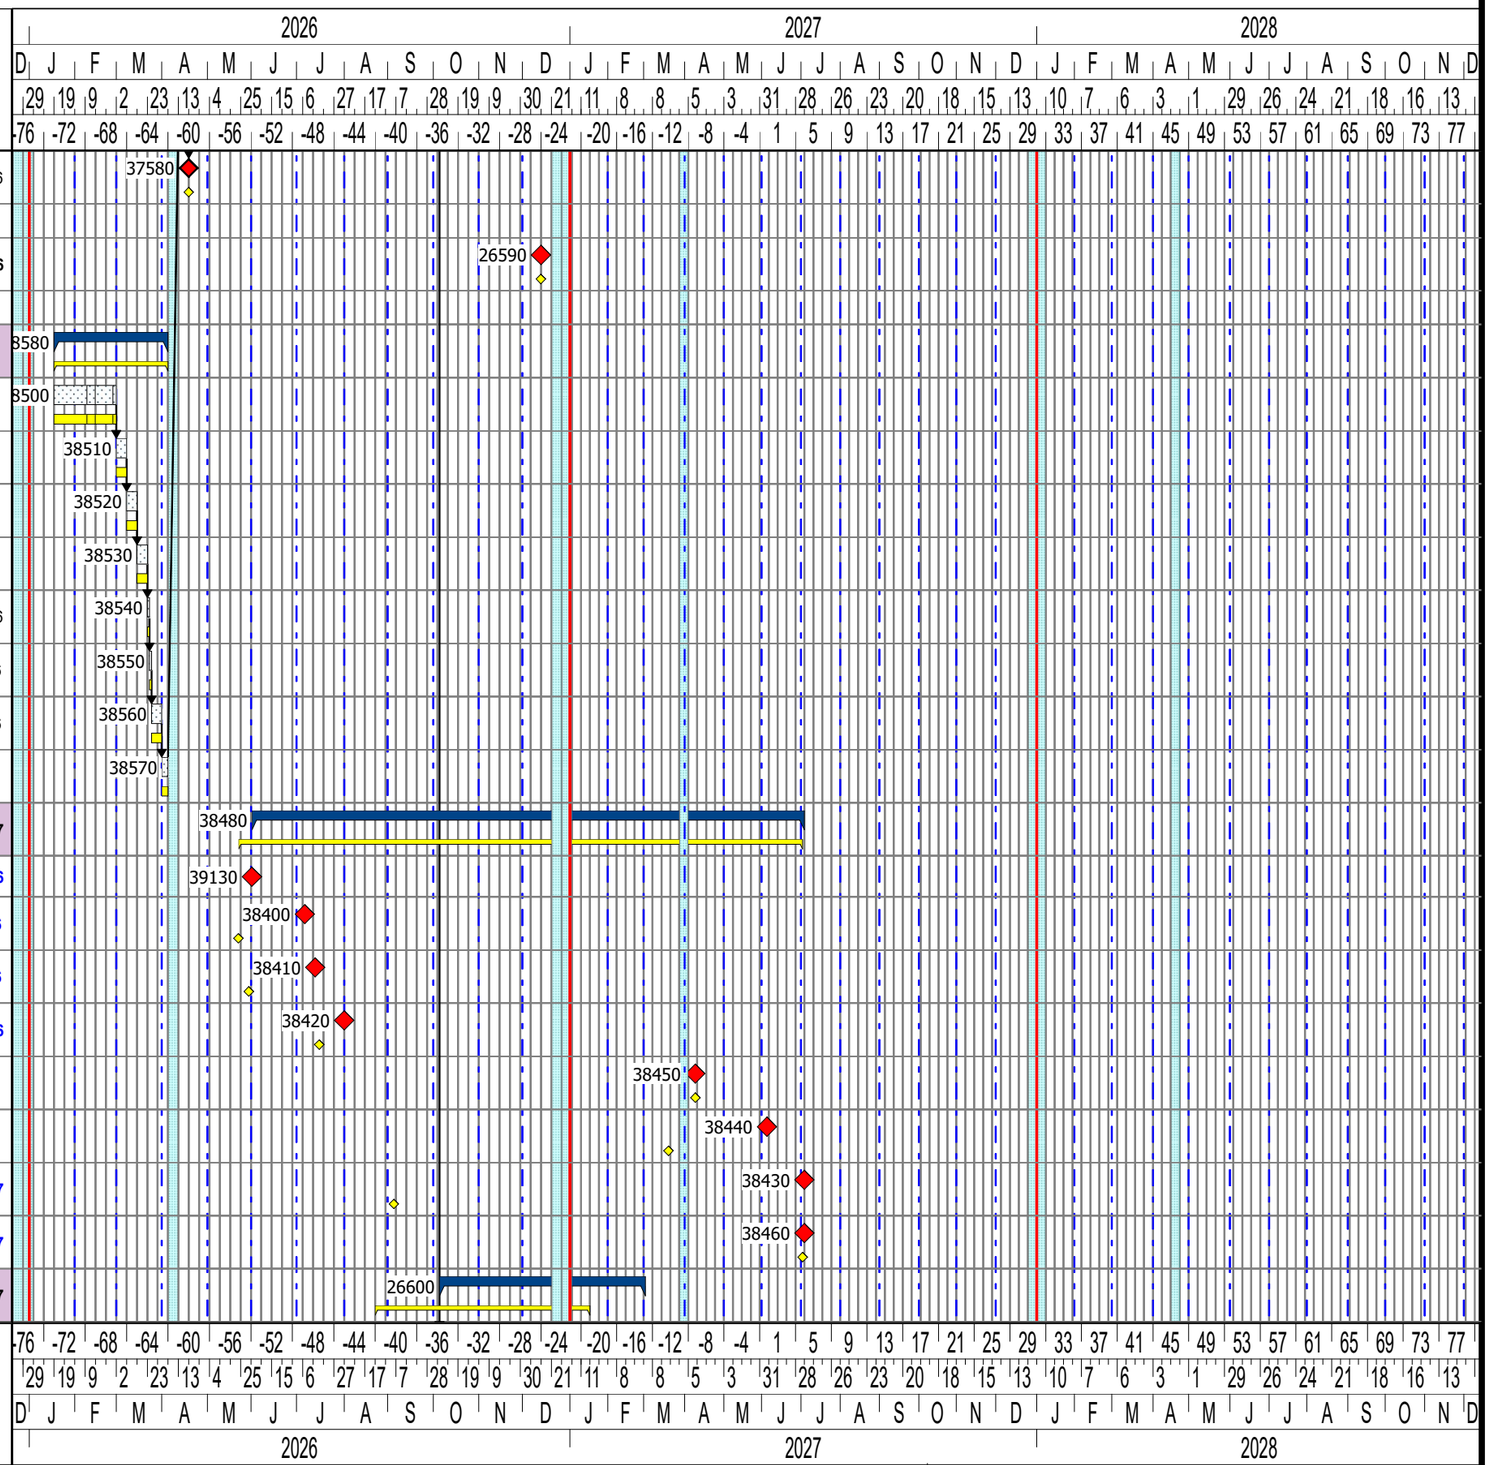

Programme No: HH0075/ST4 Draft	
Revision: REV2	Date 19/03/2026
Rev Comment:	

Christie Main Build Pre Con

Programme Status:	
Prepared For (Owner): PD	
Drawn By (Planner): LF	
Region: North West	Progress Date: 28/02/2026


'Note that the Duration Column Shows Working Weeks and Does Not Include Holidays'

INSERT TRUST LOGO HERE

Christie ASICD
Main Build Programme 02

Integrated Health Projects by VINCI BUILDING Sir Robert McALPINE

Line	Task ID (WBN)	Name	Start	Working Duration	Finish
74	**26610**	**START (Links from FBC Develoment and Approval)**	**Tue 06/10/26**		**Tue 06/10/26**
75	26540	Decommissioning (Provisional Period)	Tue 06/10/26	19w	Mon 01/03/27
76	**33600**	**Construction Programme**	**Mon 19/07/27**	**109w**	**Mon 01/10/29**
77	32620	Start on site	19 Jul 27		19 Jul 27
78	31280	Demolition (Indicative Allowance TBC)	19 Jul 27	20w	03 Dec 27
79	31490	Basement Removal (Indicative Allowance TBC)	11 Oct 27	12w	14 Jan 28
80	33610	On-Site Construction Period	Mon 06/12/27	89w	Mon 01/10/29
81	31500	Pile Mat	06 Dec 27	6w	28 Jan 28
82	31450	Piling	13 Dec 27	8w	18 Feb 28
83	31510	Drainage to Haul Road & Perimeter	24 Jan 28	7w	10 Mar 28
84	31300	Tower Crane Bases & Cure	24 Jan 28	12w	14 Apr 28
85	31160	Foundations & Underslab Drainage	24 Jan 28	15w	12 May 28
86	31170	Ground Floor Slab	20 Mar 28	11w	09 Jun 28
87	31110	Superstructure	20 Mar 28	33w	10 Nov 28
88	31180	Prop Release	24 Jul 28	14w	27 Oct 28
89	31100	Envelope	31 Jul 28	47w	13 Jul 29
90	32000	Roof Top Plant Install & Commissioning	07 May 29	12w	27 Jul 29
91	31990	Utilities/Key Services	28 Aug 28		28 Aug 28
92	31120	Fit Out	06 Nov 28	35w	27 Jul 29
93	31520	Hoist Infill (GL 2 - 3)	23 Apr 29	12w	13 Jul 29
94	31530	External Works	30 Apr 29	10w	06 Jul 29
95	31420	Project Completion	30 Jul 29	9w	01 Oct 29

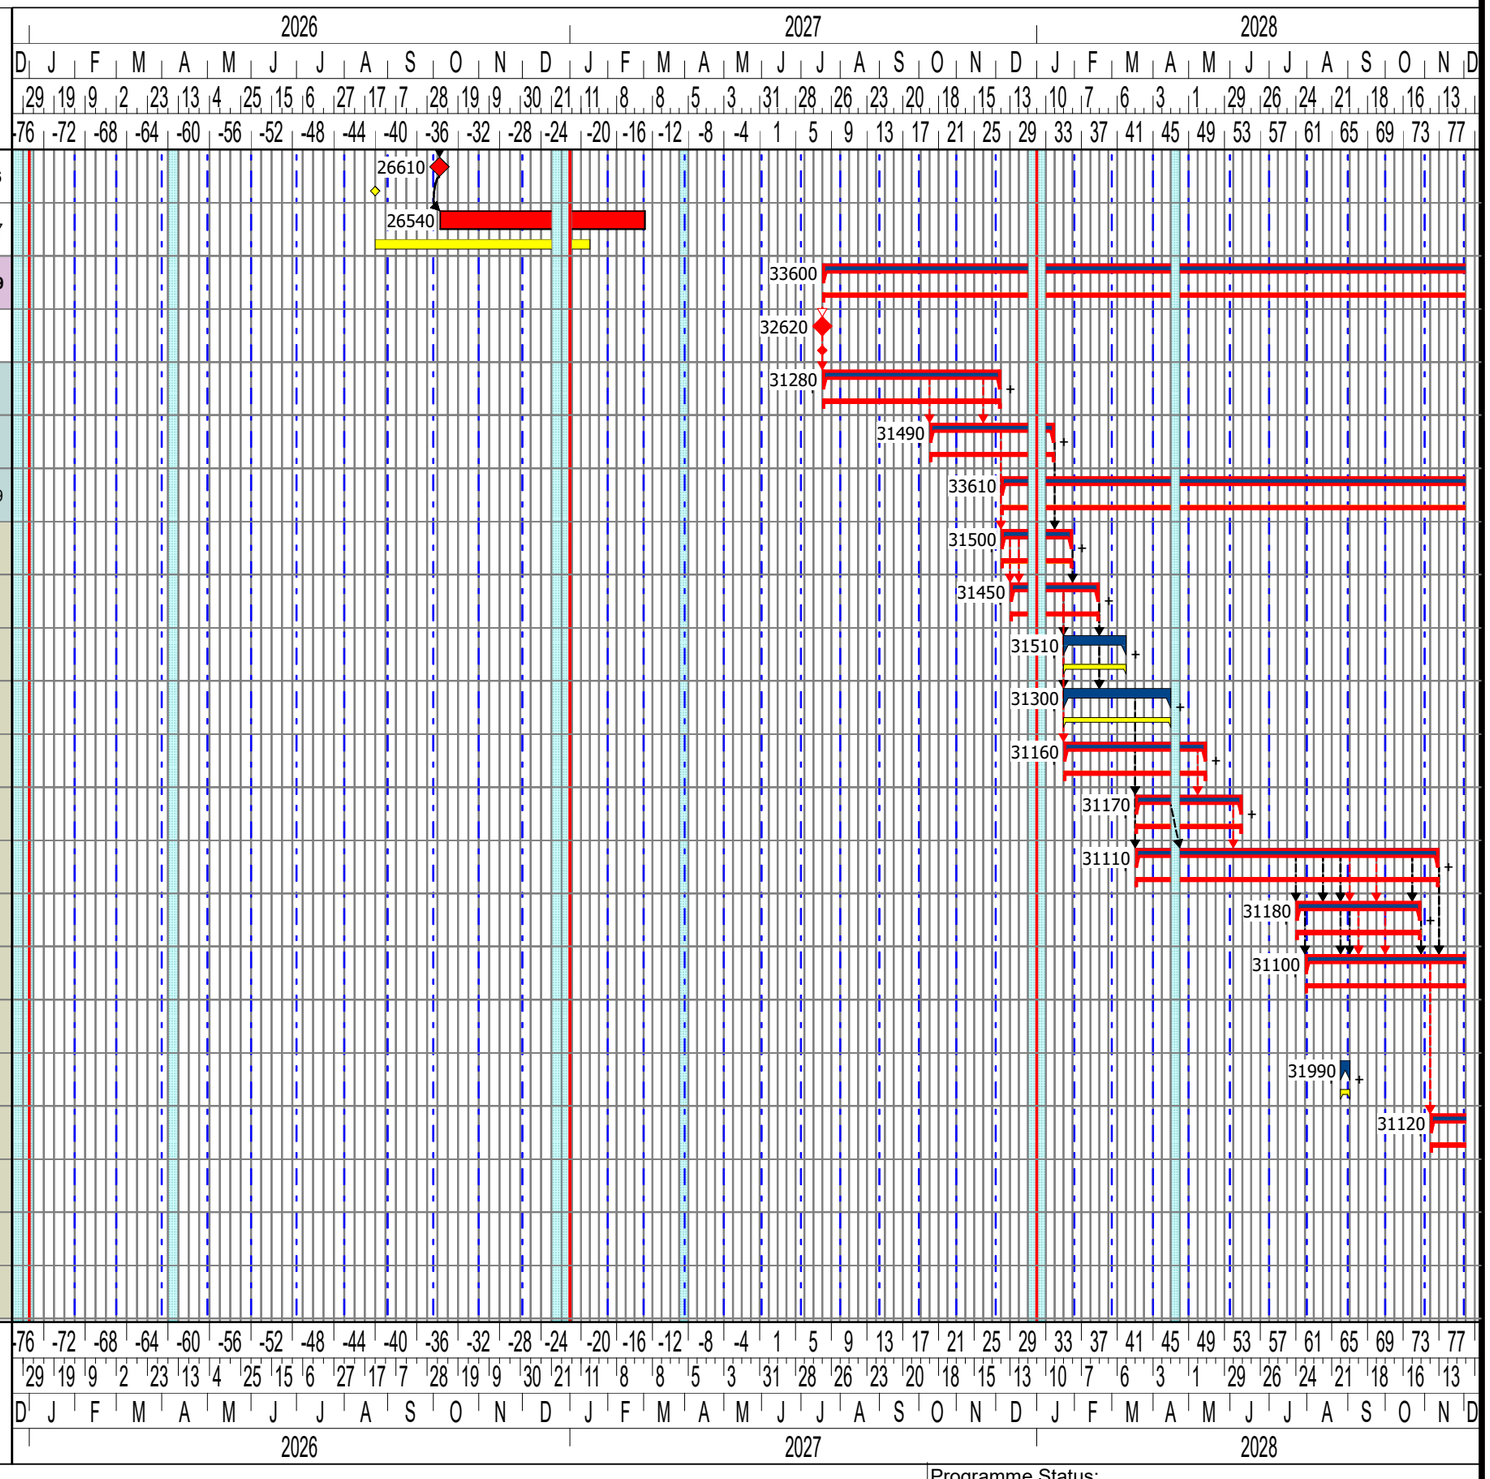

Programme No: HH0075/ST4 Draft	
Revision: REV2	Date 19/03/2026
Rev Comment:	

Christie Main Build Pre Con

Programme Status:	
Prepared For (Owner): PD	
Drawn By (Planner): LF	
Region: North West	Progress Date: 28/02/2026

'Note that the Duration Column Shows Working Weeks and Does Not Include Holidays'
