
© COPYRIGHT
The copyright in this drawing is vested in Sheppard Robson and no license or assignment of any kind has been, or is, granted to any third party whether by provision of copies or originals or otherwise unless agreed in writing.

DO NOT SCALE FROM THIS DRAWING
The contractor shall check and verify all dimensions on site and report any discrepancies in writing to Sheppard Robson before proceeding work

FOR ELECTRONIC DATA ISSUE
Electronic Data / drawings are issued as "read only" and should not be interrogated for measurement. All dimensions and levels should read, only from those values stated in text on the drawing.

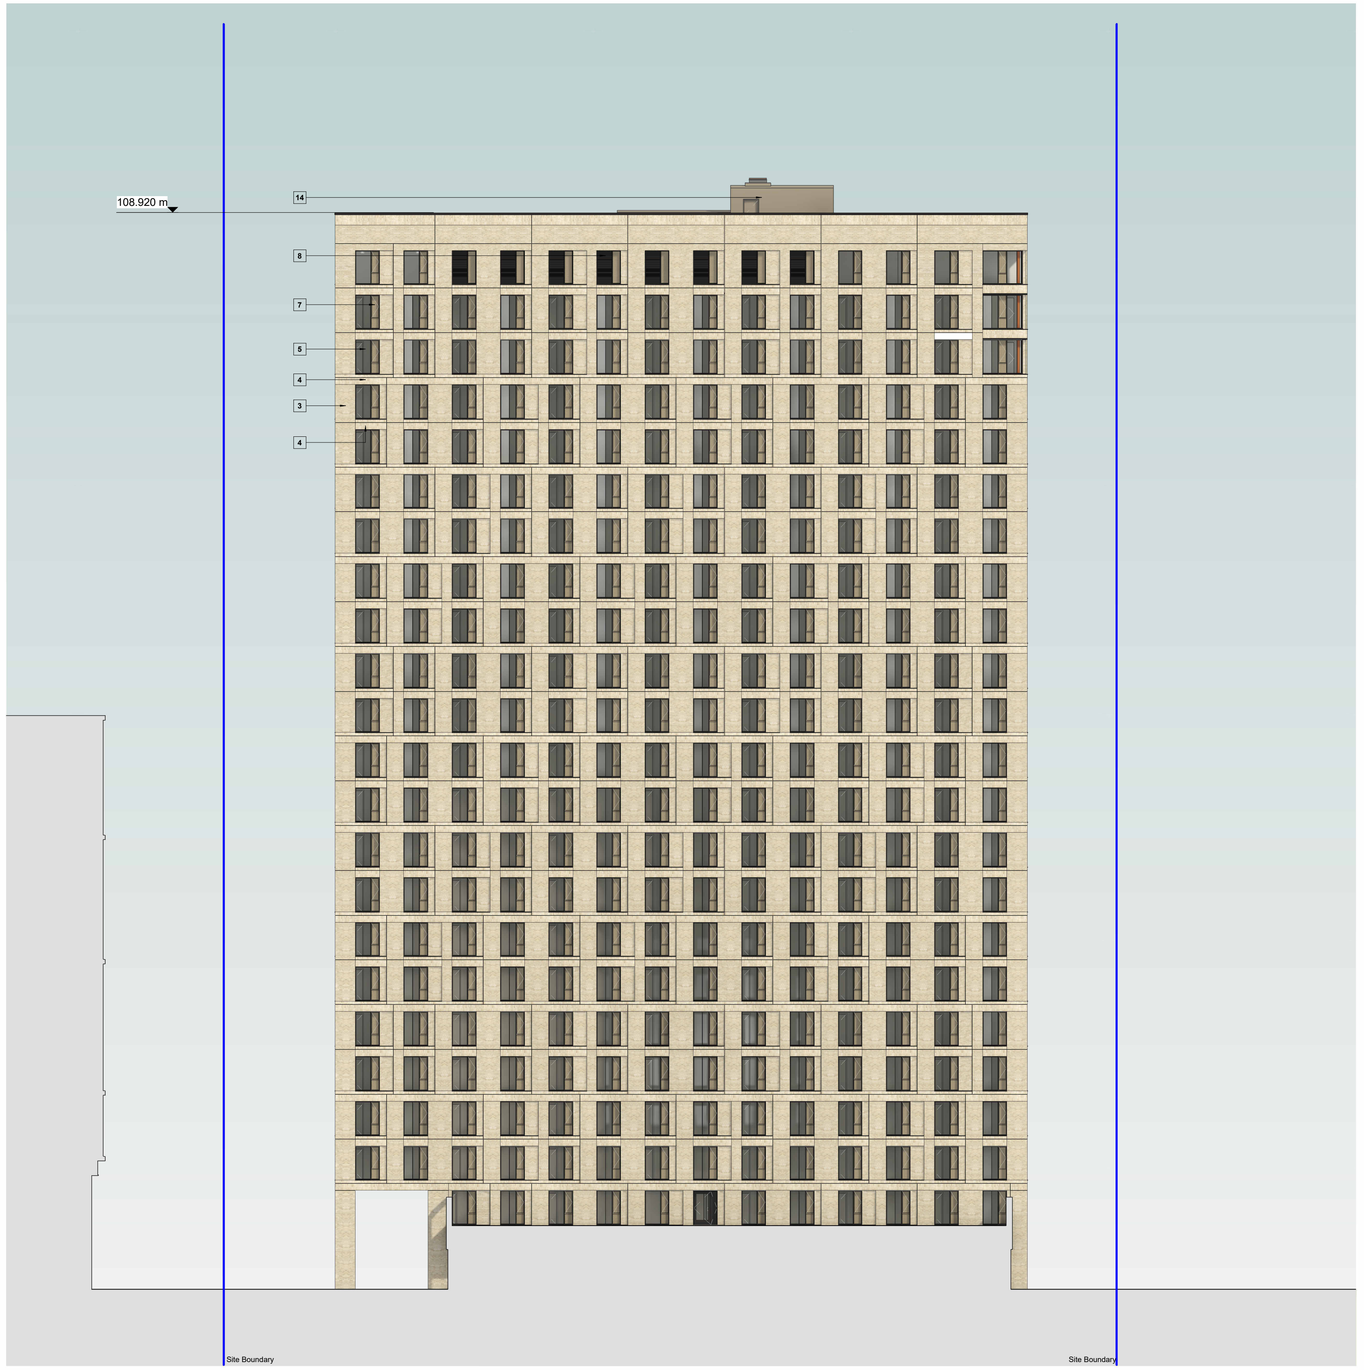

1 / 20205 **North Elevation - Amenity Deck**
1 : 200
(Referencing Sheet: 21685)

KEY

1. Red Coloured Brick - Stretcher Bond - H42/474
2. Red Coloured Brick - Soldier Course - H42/474
3. Buff Coloured Brick - Stretcher Bond - H42/475
4. Buff Coloured Brick - Soldier Course - H42/475


5. Anodized Aluminium Window System: ANO545 (KR), ANO549 (UB)
   Anodized Aluminium Window frame - L10/342, L10/343 & L10/437
6. Anodized Aluminium Window System:
   Anodized Aluminium Window Frame and Glass Panel - L10/341, L10/344, L10/345, L10/346 & L10/348
7. Bronze Coloured Anodized Aluminium Decorative Perforated Panel - L10/671
8. Bronze Aluminium Louvres (at high level) - L10/651
9. Curtain Wall: Bronze Coloured Anodized Aluminium Frame and Glass Panel - H11/111 - H11/118
10. Curtain Wall: Bronze Coloured Anodized Aluminium Frame and Back Painted Glass Insulated Panel - H11/129
11. Bronze Coloured Aluminium Insulated Panel - H11/140
12. Metal Rail Balustrade - H11/131 & H11/132
13. Aluminium Louvred Door - H11/138
14. Bronze Aluminium Cladding (at high level) - H31/124
15. Stainless Steel Dry/ Wet Riser Inlet - P20/171 & P20/172

Refer to External Finishes schedule for element colour references and locations

Indicates back painted glass

REV.	DATE	AMENDMENT
P01	24/05/2024	Stage 3 Design Freeze draft issue to support interim costing
P02	05/07/2024	Issued for Stage 3 Submission
P03	02/08/2024	WS4 technical development for subcontractor discussion
P04	16/08/2024	Stage 4 Interim Issue
P05	09/12/2024	WS4 - Update following client instruction to reduce height by 75mm per floor
P06	20/02/2025	WS4 issue

KEYPLAN



CLIENT

McLAREN PROPERTY

SHEPPARD ROBSON

77 Parkway Camden Town London NW1 7PU
T: +44 (0)20 7504 1700 E: enquiries@sheppardrobson.co.uk

PROJECT
Upper Brook Street PBSA - McLaren

SCALE@A1	DATE	ORIGINATOR	CHECKED	AUTHORISED
1 : 200	20/02/2025	RA	MT	MT

DESCRIPTION
North Elevation - Amenity Deck
Coloured GA Elevations

STAGE
Stage 4

STATUS	PURPOSE FOR ISSUE	SR NO.
S4	For Approval	6601

DRAWING NO.	REV.
MAUBS-SRA-XX-XX-DR-AR-20205	P06

Revision Notes

Drawing issued for Stage 4
