Enabling works



MCLAREN



KEY

Gate entrance

Waste skips location

Wheel wash/vehicle cleaning

Material stockpile for sampling/muck away

UBS Manchester

UBS Logistics & Phasing Document

McLaren Property

NTS

10 02 2025


- Hoarding and new gate establishment.
- Temporary welfare set up (temporary power off generator, drainage connection and water supply).
- Building demolished with arisings being segregated and removed from site.
- Site turned over to a depth of 1.5m,
- Materials stockpiled and tested in line with material management plan.
- Site area backfilled using arisings.
- Pile mat installed and compacted layers.

Information Classification: Public

Enabling works phase logistics



MCLAREN

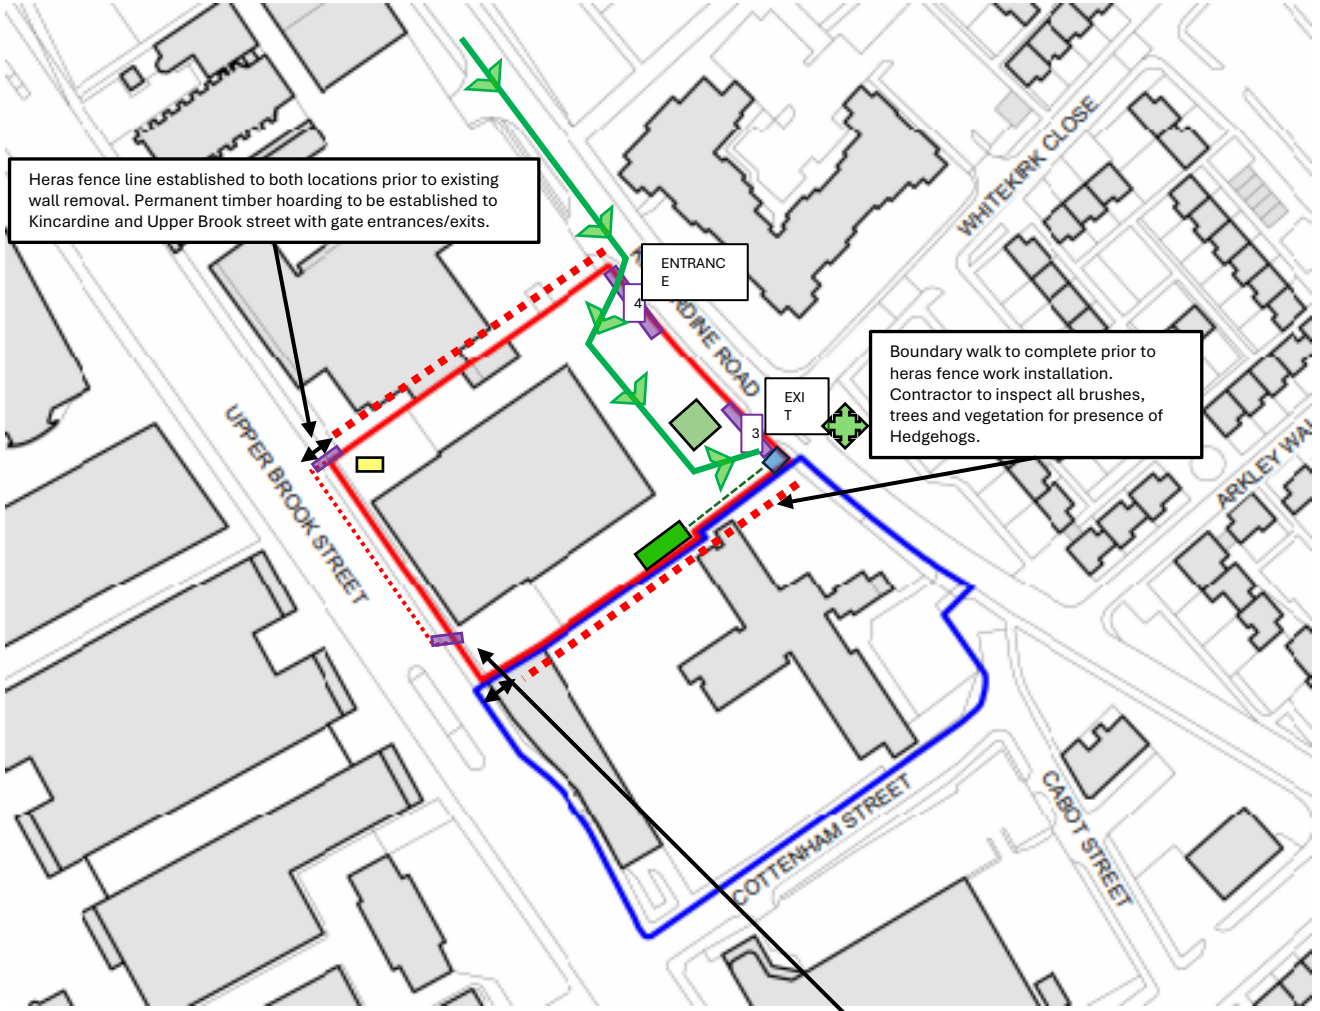

KEY

- Gate entrance
- Access / Egress Routes
- Site Accommodation
- Wheel wash/vehicle cleaning
- Hydrant for dust cannon
- Muster point
- Pedestrian access
- Pedestrian walkway

UBS Manchester


UBS Logistics & Phasing Document

McLaren Property

NTS

10 02 2025

- Hedgehog survey/inspection prior to fence works.
- Hoarding and new gate establishment.
- Temporary welfare set up (temporary power off generator, drainage connection and water supply).
- Hoarding line on Upper Brook street in line with footpath closure and single lane closure. Pedestrian route/crossing point past gate.



Information Classification: Public
