GMI Construction Group PLC	**PROJECT TITLE:** **L047 Alumno MLE -** **FOR:** **Alumno**	**PROGRAMME:** **REV: P02** **Listed Building Condition 3**	**PROGRAMME NO: P02** **ISSUED: 03/09/2024** **DRAWN: Jen Rostron** **REVISION: P02** **REV DATE:**

Line	Name	Duration	Start	Finish
	Alumno. MLE. Listed Building Consent. Condition 3a. Programme of Design Information and Samples for External Elevations			
	A programme for the issue of samples and specifications of all materials to be used on all external elevations of the development. The programme shall include timings for the submission of samples and specifications of all materials to be used on all external elevations of the development to include jointing and fixing details, details of the drips to be used to prevent staining, details of the glazing and a strategy for quality control management. (b) All samples and specifications shall			
1	Start on Site - Piling		18/11/2024	18/11/2024
2	**Quality Control Statement**	**9w 1d**	**27/09/2024**	**29/11/2024**
3	Prepare QC Statement for Project	5w 1d	27/09/2024	01/11/2024
4	Submit to Planners for Condition Discharge		04/11/2024	04/11/2024
5	Determination Period	4w	04/11/2024	29/11/2024
6	**Façade**	**13w 1d**	**30/08/2024**	**29/11/2024**
7	**Windows**	**13w 1d**	**30/08/2024**	**29/11/2024**
8	Window replacement and repair scope	2w	30/08/2024	12/09/2024
9	Meeting on site with Planners to review proposals	1w	16/09/2024	20/09/2024
10	Drawings & specifications of Windows including jointing and fixing details, details of the drips to be used to prevent staining, details of the glazing	4w 1d	20/09/2024	18/10/2024
11	Procure Window Samples	3w	14/10/2024	01/11/2024
12	Architect Heritage Statement / Condition Survey Reports	2w	21/10/2024	01/11/2024
13	Submit to Planners for Condition Discharge		04/11/2024	04/11/2024
14	Determination Period	4w	04/11/2024	29/11/2024
15	**External Walls and Doors**	**13w 1d**	**30/08/2024**	**29/11/2024**
16	External Wall replacement and repair scope	2w	30/08/2024	12/09/2024
17	Meeting on site with Planners to review proposals	1w	16/09/2024	20/09/2024
18	Drawings and specification of stucco, brick repairs, stonework and doors including jointing and fixing details, details of the drips to be used to prevent staining,	4w	23/09/2024	18/10/2024
19	Render materials samples. Procure Samples	3w 1d	11/10/2024	01/11/2024
20	Cills samples. Procure Samples	3w 1d	11/10/2024	01/11/2024
21	Architect Heritage Statement / Condition Survey Reports	2w	21/10/2024	01/11/2024
22	Submit to Planners for Condition Discharge		04/11/2024	04/11/2024
23	Determination Period	4w	04/11/2024	29/11/2024
24	**Roof Coverings and Structure**	**11w**	**24/09/2024**	**09/12/2024**
25	Roof replacement and structural repair scope	2w	24/09/2024	07/10/2024
26	Meeting on site with Planners to review proposals	1w	09/10/2024	15/10/2024
27	Drawings and specification of stucco, brick repairs, stonework and doors including jointing and fixing details, details of the drips to be used to prevent staining,	4w	15/10/2024	11/11/2024
28	Tile Samples	2w	29/10/2024	11/11/2024
29	Leadwork Samples	2w	29/10/2024	11/11/2024
30	Architect Heritage Statement / Condition Survey Reports	2w	29/10/2024	11/11/2024
31	Submit to Planners for Condition Discharge		12/11/2024	12/11/2024
32	Determination Period	4w	12/11/2024	09/12/2024
33	**BSR & Construction Activities**	**29w 1d**	**14/11/2024**	**26/06/2025**
34	BSR Submission Date for Listed Building		14/11/2024	14/11/2024
35	Lead In	18w 4d	09/12/2024	06/05/2025
36	Roofing Start on Site		08/05/2025	08/05/2025
37	Façade Start on Site		26/06/2025	26/06/2025

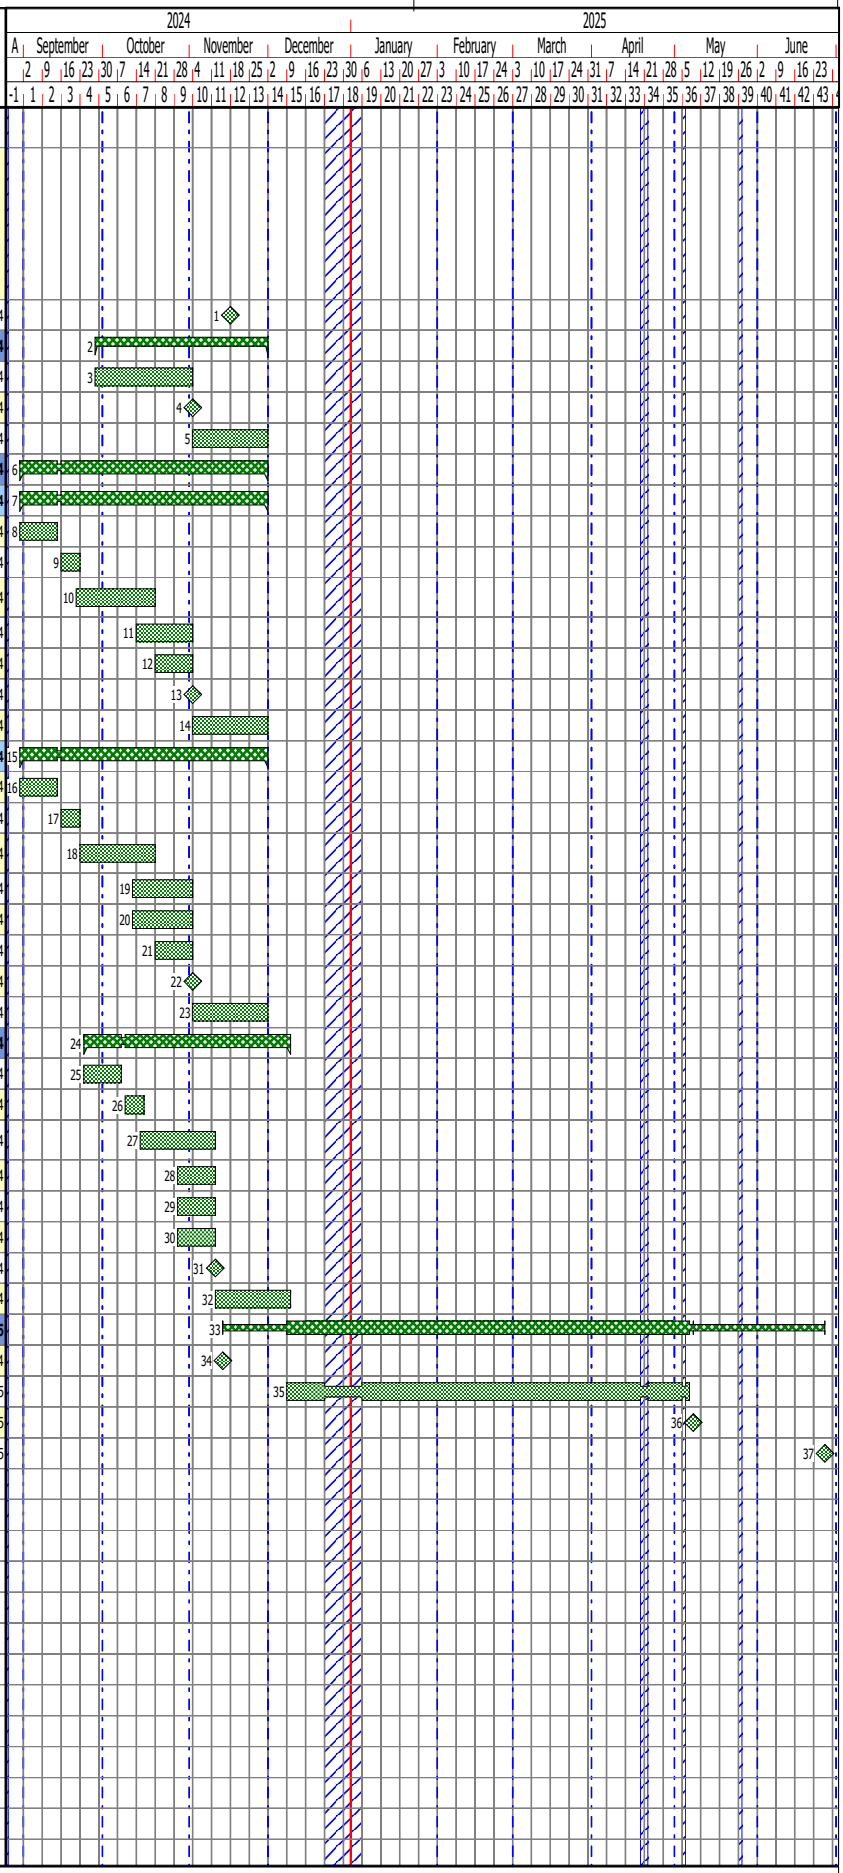

Milestone Appearances

◇ Start Milestone
