
35 Fountain Street - Visual Facade Mock Up Programme

for

Bywater Properties

Line	Name	Start	Duration	Finish
1	**Facade Mock Up Programme**	**08 Sep 25**	**32w 3d**	**12 May 26**
2	**Sample Procurement**	**08 Sep 25**	**10w**	**14 Nov 25**
3	**Windows (incl. Louvre Grill & Aluminium Cill)**	**08 Sep 25**	**10w**	**14 Nov 25**
4	Place Order	08 Sep 25	1w	12 Sep 25
5	Lead In Time	15 Sep 25	9w	14 Nov 25
6	**Concrete String Course**	**15 Sep 25**	**9w**	**14 Nov 25**
7	Place Order	15 Sep 25	1w	19 Sep 25
8	Lead In Time	22 Sep 25	8w	14 Nov 25
9	**Brick (incl. Masonry Support, Lintel)**	**15 Sep 25**	**9w**	**14 Nov 25**
10	Place Order	15 Sep 25	1w	19 Sep 25
11	Lead In Time	22 Sep 25	8w	14 Nov 25
12	**SFS**	**22 Sep 25**	**8w**	**14 Nov 25**
13	Place Order	22 Sep 25	1w	26 Sep 25
14	Lead In Time	29 Sep 25	7w	14 Nov 25
15	**Facade Mock Up Construction**	**17 Nov 25**	**3w**	**05 Dec 25**
16	Installation On Site (2mx2m panel)	17 Nov 25	3w	05 Dec 25
17	**Inspection & Approval Period**	**08 Dec 25**	**9w**	**20 Feb 26**
18	Planner's Inspection(s)	08 Dec 25	1w	12 Dec 25
19	Facade Mock Up Verbal Approval	15 Dec 25	0w	15 Dec 25
20	Facade Mock Up Formal Approval Period	15 Dec 25	8w	20 Feb 26
21	Client Instruction to Proceed based on Informal Planning Approval	16 Dec 25	0w	16 Dec 25
22	**Site Works Key Milestones**	**01 Dec 25**	**20w 3d**	**12 May 26**
23	Site Possession & Establishment Start	01 Dec 25	0w	01 Dec 25
24	Permanent Works (Ex Bldg Steel Strengthening/Alterations) Start	19 Jan 26	0w	19 Jan 26
25	Facade Preparation Works (Masonry Support) Start	20 Feb 26	0w	20 Feb 26
26	PCC Stringer Start	31 Mar 26	0w	31 Mar 26
27	Windows Installation Start	13 Apr 26	0w	13 Apr 26
28	Brickwork Start	12 May 26	0w	12 May 26

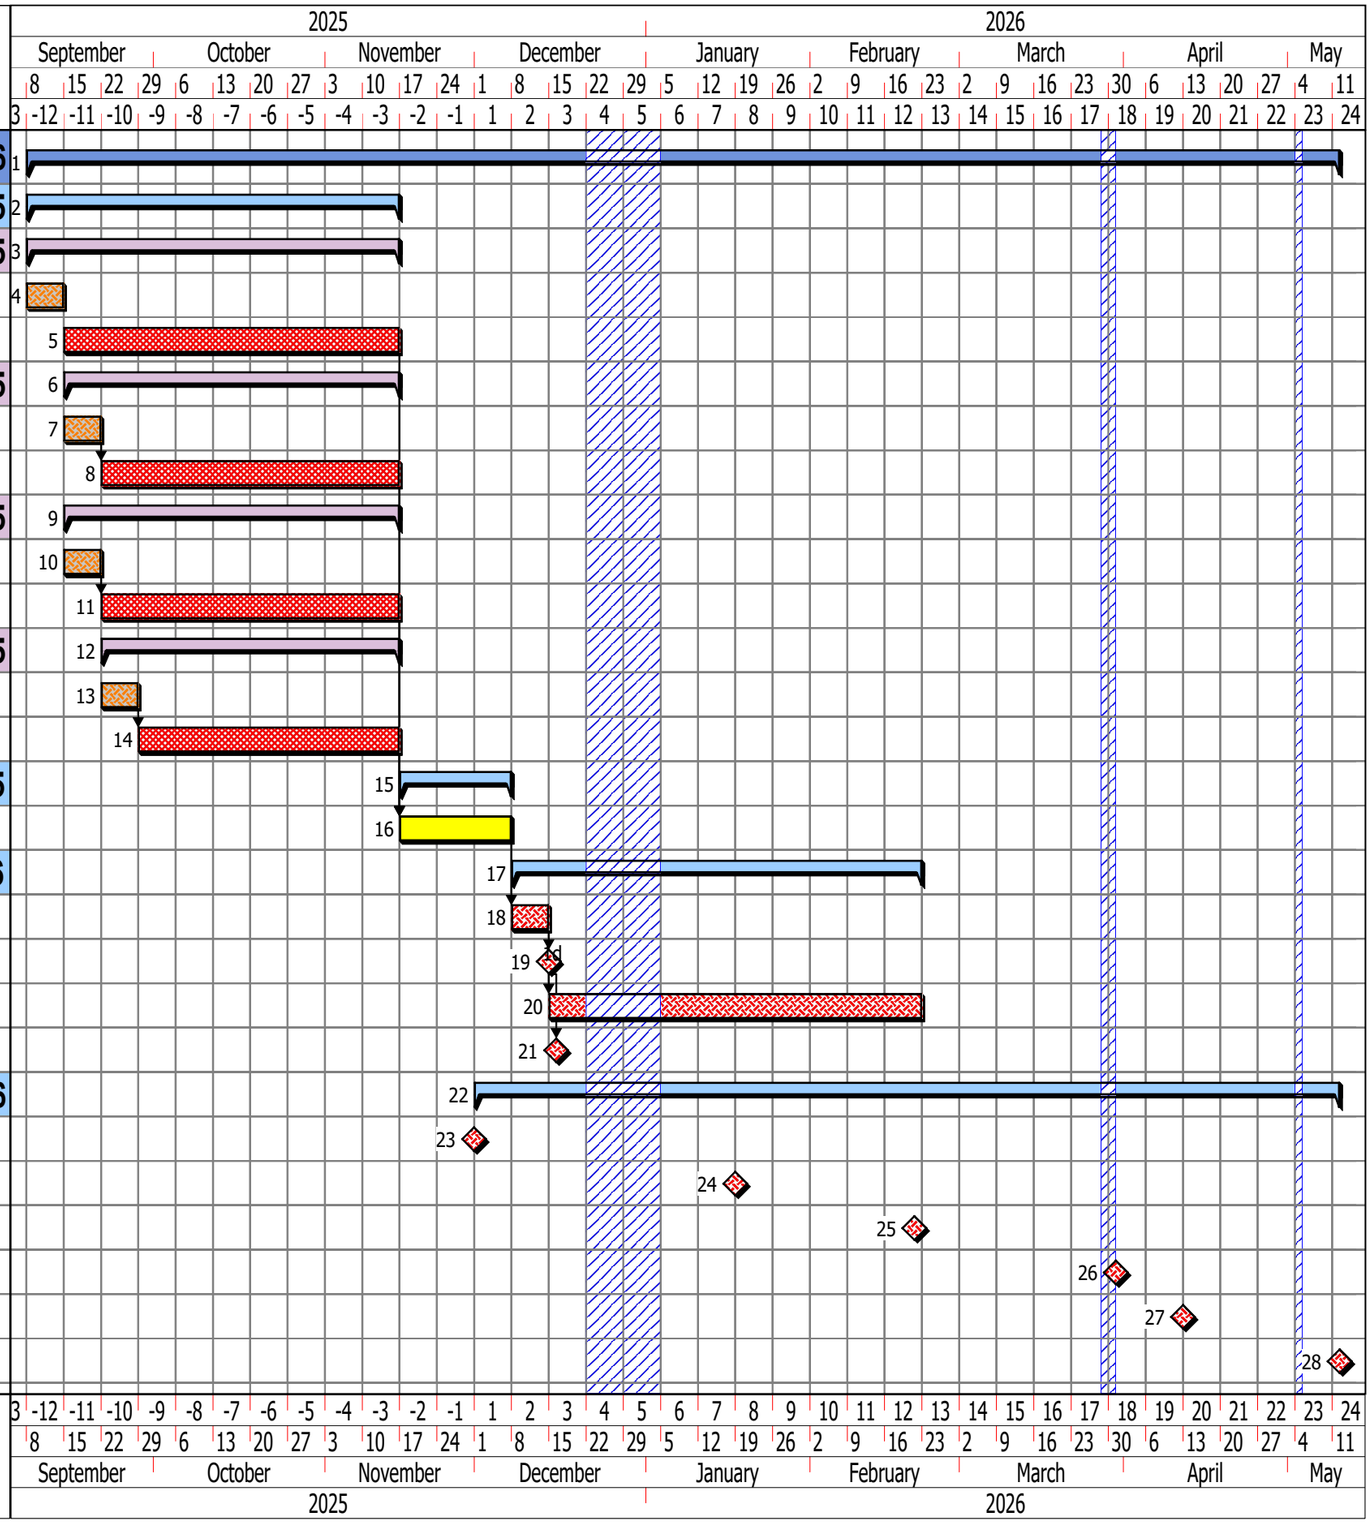

Programme No.: Facade Mock Up
Revision:
Issue Date: 03/09/2025
Revision Date:
Notes:
Contract No.:
Drawn by: Vitaliy Sydoruk

File :- C:\Users\vitaliy.sydoruk\OneDrive - GMI Construction\Documents\GMI\Projects\08 35 Fountain St\Programme\Build Programme\Darft\35 Fountain Street - Tender Programme.pp
