
Hotel Gotham CP Installation

Outline Programme

ID	Task Name	Duration	Start	Finish
1	**Mobilisation**	**5 days**	**Mon 06/01/25**	**Fri 10/01/25**
2	Site Compound & TM	5 days	Mon 06/01/25	Fri 10/01/25
3	**Spring Gardens Elevation**	**100 days**	**Mon 13/01/25**	**Thu 05/06/25**
4	Erect Scaffold	20 days	Mon 13/01/25	Fri 07/02/25
5	External CP Works / Stone Repairs (Zone 13)	14 days	Mon 27/01/25	Thu 13/02/25
6	External CP Works / Stone Repairs (Zone 14)	16 days	Fri 14/02/25	Fri 07/03/25
7	External CP Works / Stone Repairs (Zone 15)	15 days	Mon 10/03/25	Fri 28/03/25
8	External CP Works / Stone Repairs (Zone 16)	15 days	Mon 31/03/25	Tue 22/04/25
9	Test/Commission	15 days	Wed 23/04/25	Wed 14/05/25
10	Dismantle Scaffold	15 days	Thu 15/05/25	Thu 05/06/25
11	**King Street Elevation**	**102 days**	**Mon 24/03/25**	**Mon 18/08/25**
12	Erect Scaffold	20 days	Mon 24/03/25	Tue 22/04/25
13	External CP Works / Stone Repairs (Zone 1)	12 days	Wed 23/04/25	Fri 09/05/25
14	External CP Works / Stone Repairs (Zone 2)	14 days	Mon 12/05/25	Fri 30/05/25
15	External CP Works / Stone Repairs (Zone 3)	13 days	Mon 02/06/25	Wed 18/06/25
16	External CP Works / Stone Repairs (Zone 4)	13 days	Thu 19/06/25	Mon 07/07/25
17	Test/Commission	15 days	Tue 08/07/25	Mon 28/07/25
18	Dismantle Scaffold	15 days	Tue 29/07/25	Mon 18/08/25
19	**Brown Street Elevation**	**111 days**	**Tue 10/06/25**	**Wed 12/11/25**
20	Erect Scaffold	20 days	Tue 10/06/25	Mon 07/07/25
21	External CP Works / Stone Repairs (Zone 5)	15 days	Tue 08/07/25	Mon 28/07/25
22	External CP Works / Stone Repairs (Zone 6)	16 days	Tue 29/07/25	Tue 19/08/25
23	External CP Works / Stone Repairs (Zone 7)	15 days	Wed 20/08/25	Wed 10/09/25
24	External CP Works / Stone Repairs (Zone 8)	15 days	Thu 11/09/25	Wed 01/10/25
25	Test/Commission	15 days	Thu 02/10/25	Wed 22/10/25
26	Dismantle Scaffold	15 days	Thu 23/10/25	Wed 12/11/25
27	**Chancery Lane Elevation**	**92 days**	**Thu 04/09/25**	**Fri 23/01/26**
28	Erect Scaffold	20 days	Thu 04/09/25	Wed 01/10/25
29	External CP Works / Stone Repairs (Zone 9)	12 days	Thu 02/10/25	Fri 17/10/25
30	Test/Commission (Zone 9)	5 days	Mon 20/10/25	Fri 24/10/25
31	External CP Works / Stone Repairs (Zone 10)	14 days	Mon 20/10/25	Thu 06/11/25
32	Test/Commission (Zone 10)	5 days	Fri 07/11/25	Thu 13/11/25
33	External CP Works / Stone Repairs (Zone 11)	13 days	Fri 07/11/25	Tue 25/11/25
34	Test/Commission (Zone 11)	5 days	Wed 26/11/25	Tue 02/12/25
35	External CP Works / Stone Repairs (Zone 12)	13 days	Wed 26/11/25	Fri 12/12/25
36	Test/Commission (Zone 12)	5 days	Mon 15/12/25	Fri 19/12/25
37	Dismantle Scaffold	15 days	Mon 05/01/26	Fri 23/01/26
38	**Demobilisation**	**5 days**	**Mon 26/01/26**	**Fri 30/01/26**
39	Remove Site Compound	5 days	Mon 26/01/26	Fri 30/01/26
40				
41	**Scaffold Embargo**	25 days	Mon 17/11/25	Fri 19/12/25
42	**Special Event (Spring Gardens)**	1 day		

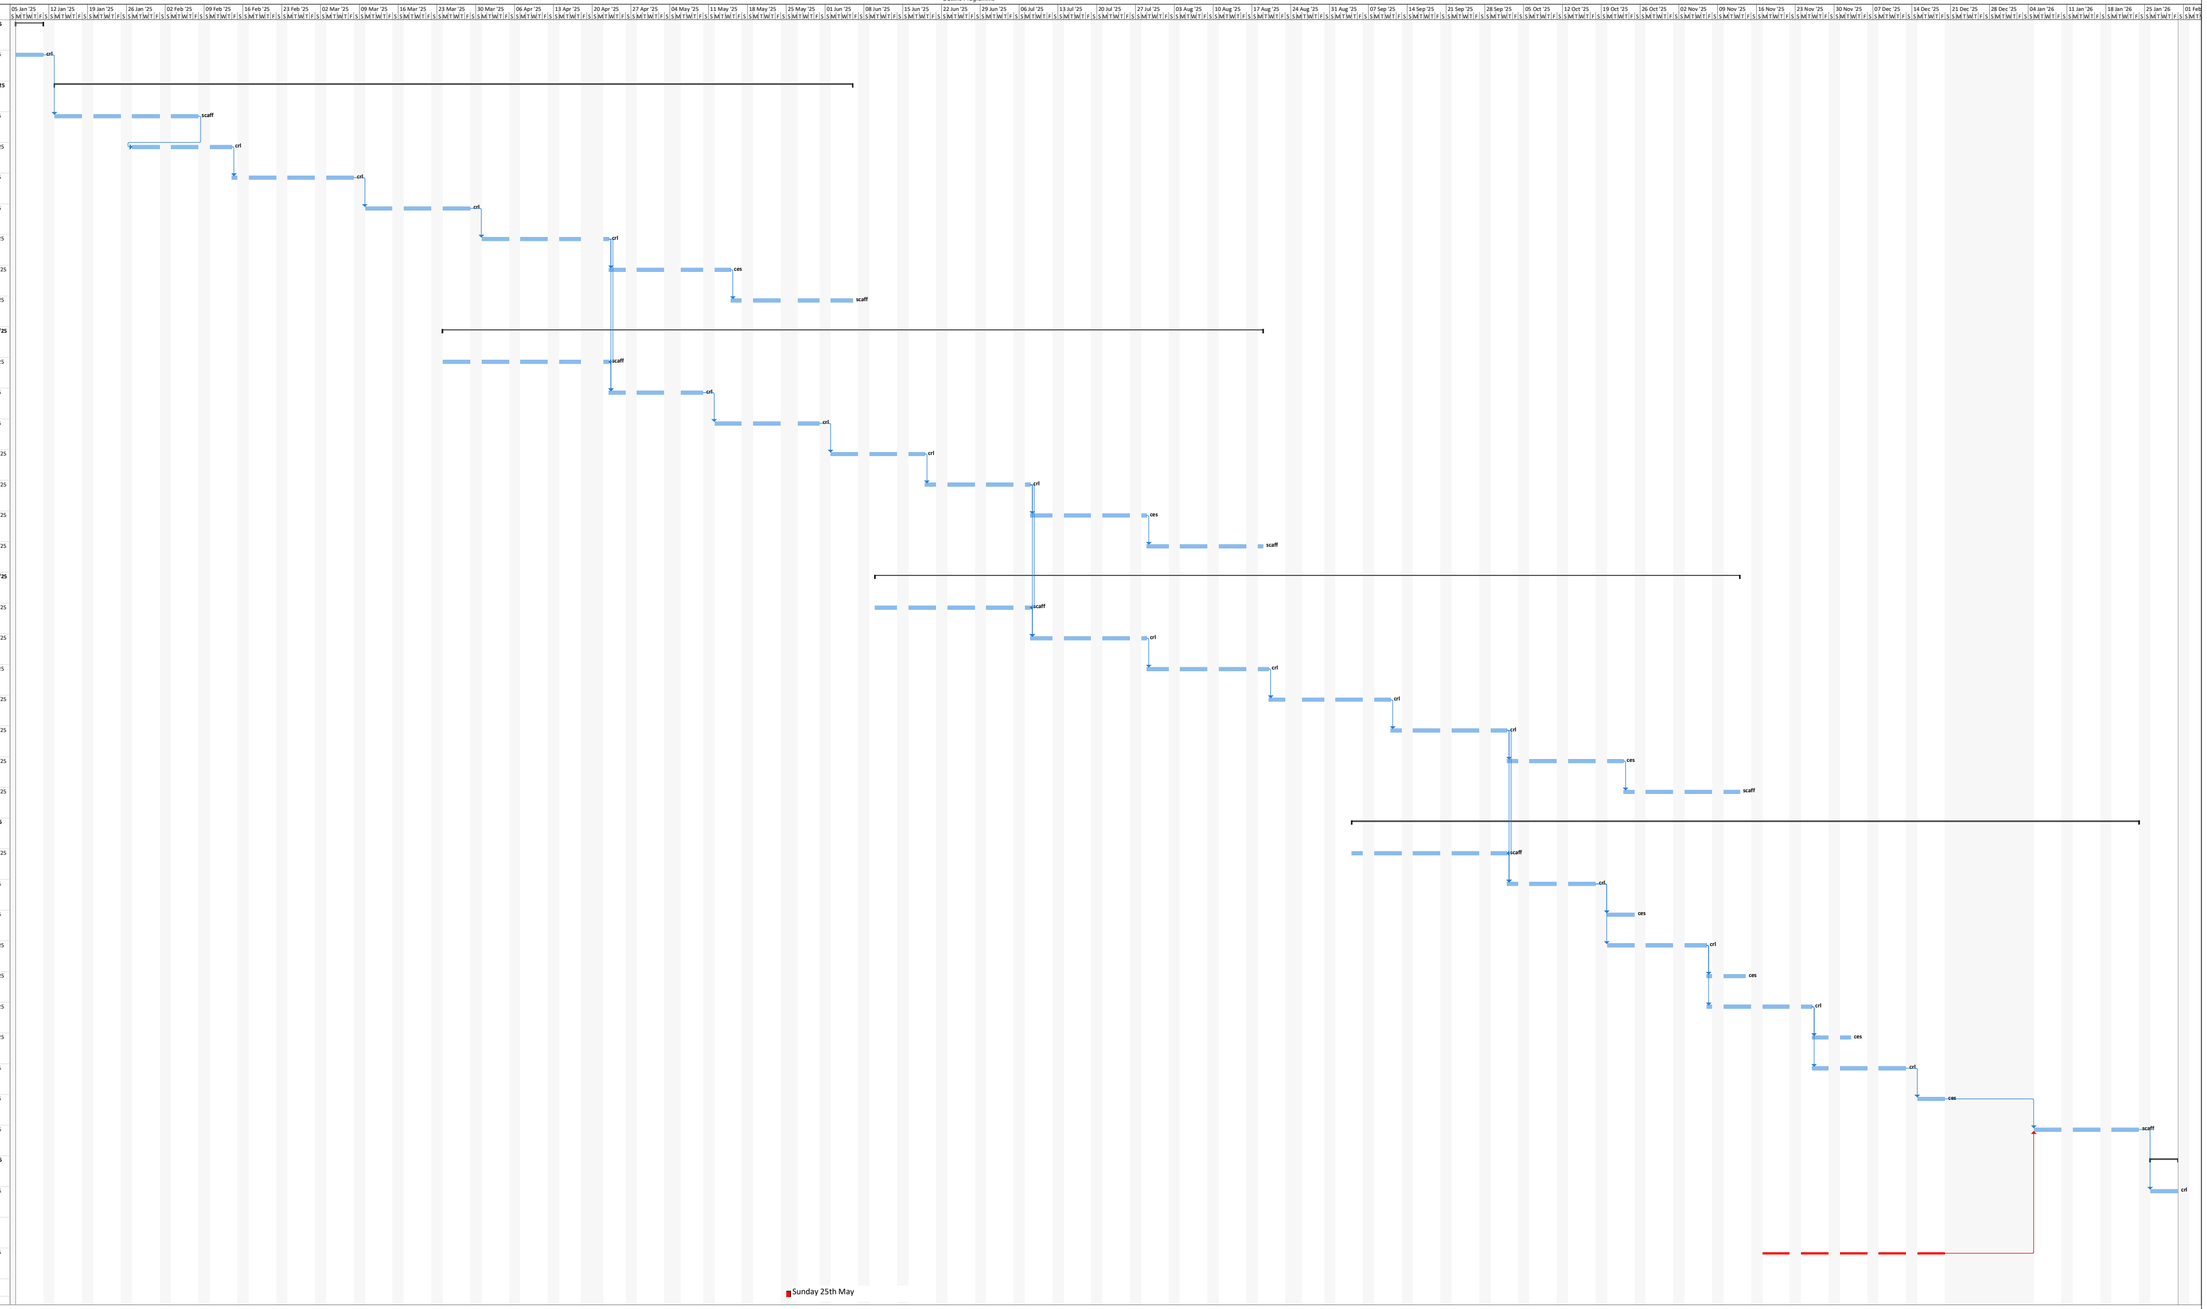

Project: mspro11
Date: Tue 03/12/24

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress | Manual Progress
