
Line	Description	Start	Finish	Working Duration
1	Appointment of Artelier	20/11/2023 *	20/11/2023	
2	Phase A - Public Art Strategy (4-6 weeks)	20/11/2023	12/01/2024	6w
3	Phase B - Project Kick Off & Research (6-8 weeks)	15/01/2024	08/03/2024	8w
4	Phase C - Proposal Development (4-8 weeks)	11/03/2024	08/05/2024	8w
5	Phase D - Artist Engagement (4-8 Weeks)	09/05/2024	04/07/2024	8w
6	Phase E - Artwork Commissioning (30-60 weeks)	05/07/2024	25/10/2024	16w
	*Phase E assumes Design/Manufacture of panels (TBC)			
7	Sample Production	02/09/2024	25/10/2024	8w
8	Issue of sample to MCC	28/10/2024	28/10/2024	
9	Approval Period	28/10/2024	17/01/2025	10w
10	Design / Procurement / Manufacture of precast panels	20/01/2025	18/12/2025	46w 4d

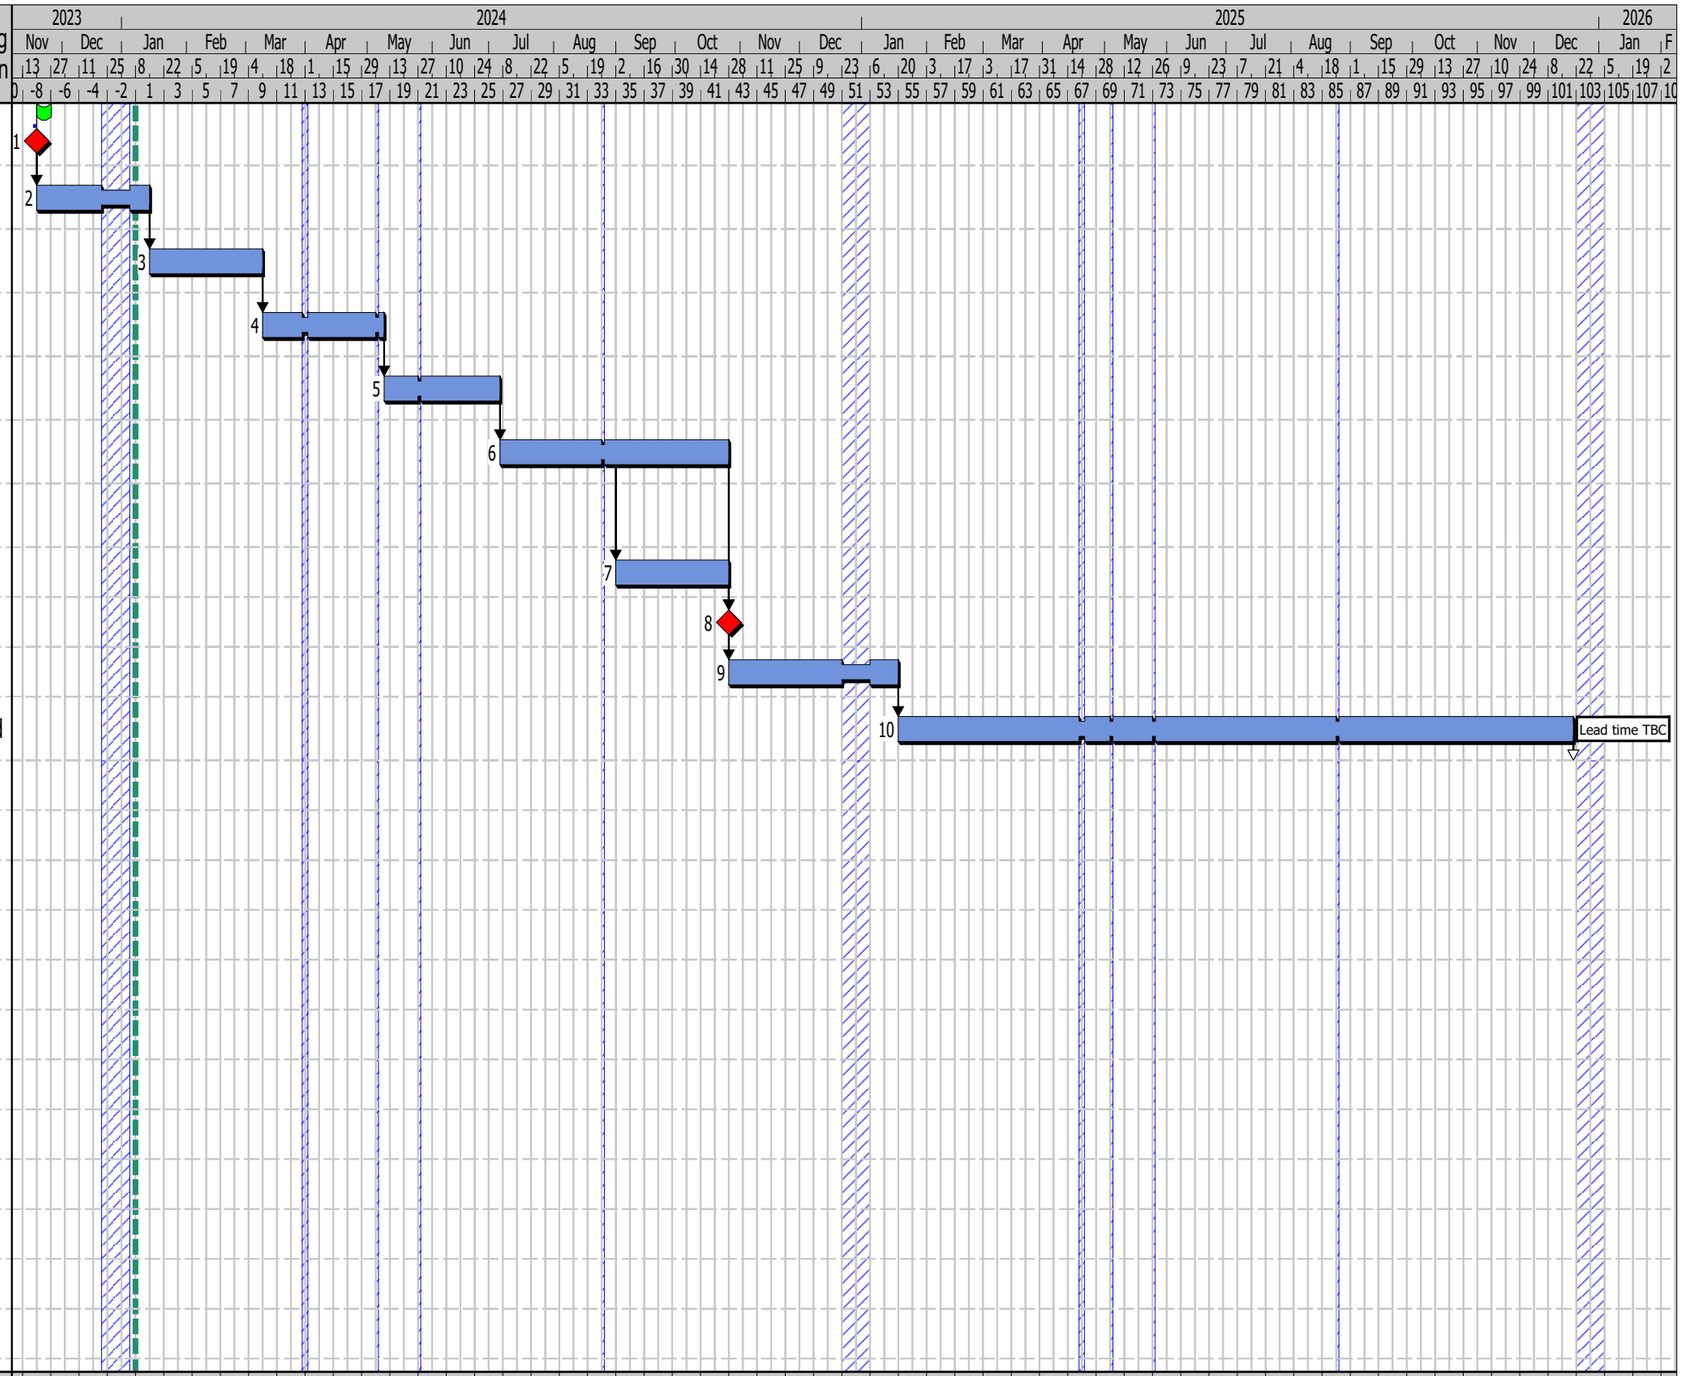

Line Description Start Finish Working Duration

Head Office:
4 Abbey Wood Road
Kings Hill
West Malling
Kent
ME19 4AB

Tel: 01732 526 850

Notes:

One Medlock Street, Manchester

Dominvs

Precast Panels / Art Wall

Programme No: 00001 Rev: PCSA (R6)

Drawn: RN | Checked: | Date: 26/09/2023
